





ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 26, '26							May 3, '26		
									S	M	T	W	T	F	S	S	M	T
1			Preparation and logistics of the project.	12 days	Mon 4/27/26	Tue 5/12/26												
2			Planning and Site Assessment.	5 days	Mon 4/27/26	Fri 5/1/26												
3			Check on all painting sections.	1 day	Mon 4/27/26	Mon 4/27/26												
4			Accept paint and material specifications of color.	1 day	Tue 4/28/26	Tue 4/28/26	3											
5			Snapshots of the status quo.	1 day	Wed 4/29/26	Wed 4/29/26	4											
6			Develop a detailed boom lift plan of action.	1 day	Thu 4/30/26	Thu 4/30/26	5											
7			Procuring Material and Equipment.	1 day	Mon 5/4/26	Mon 5/4/26	2											
8			Purchase Sherwin-Williams paint (primers and finish coats).	2 days	Mon 4/27/26	Tue 4/28/26												
9			Use secure trays, rollers, drop cloths, and brushes.	1 day	Wed 4/29/26	Wed 4/29/26	8											

Project: Lyle Public Schools Inte Date: Mon 4/27/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

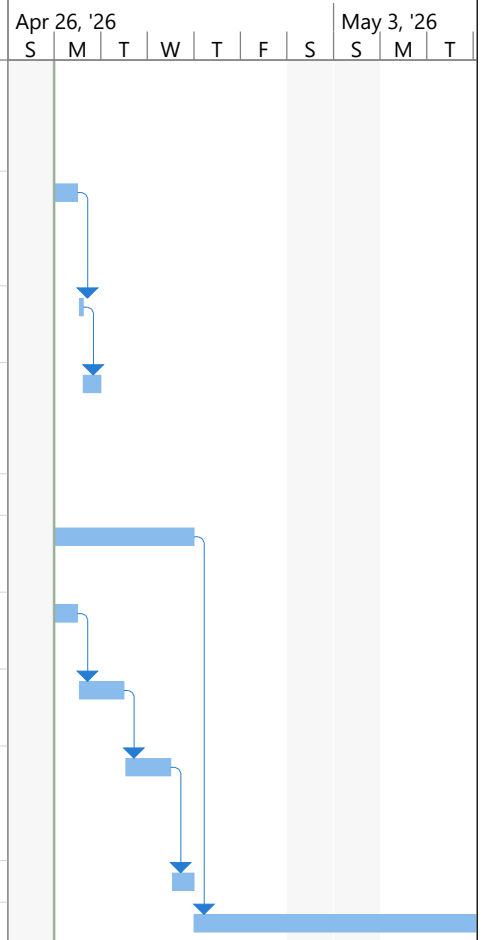
ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 26, '26							May 3, '26		
									S	M	T	W	T	F	S	S	M	T
10			book boom lift equipment.	1 day	Thu 4/30/26	Thu 4/30/26	9											
11			Purchase cleaning supplies and protective supplies.	1 day	Fri 5/1/26	Fri 5/1/26	10											
12			Site Preparation	5 days	Tue 5/5/26	Mon 5/11/26	7											
13			Flood to ward and cover fixtures.	2 days	Mon 4/27/26	Tue 4/28/26												
14			Mobility or relocation of furniture and equipment.	2 days	Wed 4/29/26	Thu 4/30/26	13											
15			Install dust containment and ventilation systems.	1 day	Fri 5/1/26	Fri 5/1/26	14											
16			Main Entry and Hallways Painted.	14 days	Tue 5/12/26	Fri 5/29/26	12											
17			Surface Preparation, main	3 days	Mon 4/27/26	Wed 4/29/26												
18			Wipe down walls with dirt and grime.	1 day?	Mon 4/27/26	Mon 4/27/26												
19			Scried and sand-edged spots.	1 day?	Tue 4/28/26	Tue 4/28/26	18											
20			Fix a hole and a crack.	0.5 days	Wed 4/29/26	Wed 4/29/26	19											



Project: Lyle Public Schools Inte Date: Mon 4/27/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 26, '26							May 3, '26		
					S	M	T	W	T	F	S	S	M	T				
21			Prim prime spot areas.	0.5 days	Wed 4/29/26	Wed 4/29/26	20											
22			Main Entry Painting	4 days	Thu 4/30/26	Tue 5/5/26	17											
23			First coat of ceiling paint.	1 day	Mon 4/27/26	Mon 4/27/26												
24			Apply a base coat of paint to the walls.	1 day	Tue 4/28/26	Tue 4/28/26	23											
25			Paint a second coat of paint on ceilings.	1 day	Wed 4/29/26	Wed 4/29/26	24											
26			Paint a second coat on the walls.	0.5 days	Thu 4/30/26	Thu 4/30/26	25											
27			Painting inside door	0.5 days	Thu 4/30/26	Thu 4/30/26	26											
28			Surface Premediation of Hallways.	2 days	Wed 5/6/26	Thu 5/7/26	22											
29			Wash, scrape, sand, and repair hallway walls.	1.5 days	Mon 4/27/26	Tue 4/28/26												
30			Apply spot priming.	0.5 days	Tue 4/28/26	Tue 4/28/26	29											
31			Hallway Painting (Phase 1)	3 days	Fri 5/8/26	Tue 5/12/26	28											
32			First paint the wall.	1.5 days	Mon 4/27/26	Tue 4/28/26												
33			Coat the walls again with paint.	1.5 days	Tue 4/28/26	Wed 4/29/26	32											


Project: Lyle Public Schools Inte Date: Mon 4/27/26		Task		Inactive Summary		External Tasks	
		Split		Manual Task		External Milestone	
		Milestone		Duration-only		Deadline	
		Summary		Manual Summary Rollup		Progress	
		Project Summary		Manual Summary		Manual Progress	
		Inactive Task		Start-only			
		Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 26, '26	S	M	T	W	T	F	S	May 3, '26	S	M	T
34			Main Entry and Hallways Quality Inspection	1 day	Wed 5/13/26	Wed 5/13/26	31													
35			Make a visual observation of paint coverage.	0.5 days	Mon 4/27/26	Mon 4/27/26														
36			Check color and finish.	0.25 days	Mon 4/27/26	Mon 4/27/26	35													
37			The project records and the completion of documentation.	0.25 days	Mon 4/27/26	Mon 4/27/26	36													
38			Gym Walls Painted	10 days	Thu 5/14/26	Wed 5/27/26	34													
39			Gym Wall Preparation.	3 days	Mon 4/27/26	Wed 4/29/26														
40			Install a high-wall access boom lift.	0.5 days	Mon 4/27/26	Mon 4/27/26														
41			Clean all gym wall surfaces.	1 day?	Mon 4/27/26	Tue 4/28/26	40													
42			Scrape and sand and patch up areas that have been	1 day?	Tue 4/28/26	Wed 4/29/26	41													
43			Apply spot priming.	0.5 days	Wed 4/29/26	Wed 4/29/26	42													
44			Gym Wall Painting	5 days	Thu 4/30/26	Wed 5/6/26	39													




Project: Lyle Public Schools Inte Date: Mon 4/27/26		Task		Inactive Summary		External Tasks	
		Split		Manual Task		External Milestone	
		Milestone		Duration-only		Deadline	
		Summary		Manual Summary Rollup		Progress	
		Project Summary		Manual Summary		Manual Progress	
		Inactive Task		Start-only			
		Inactive Milestone		Finish-only			

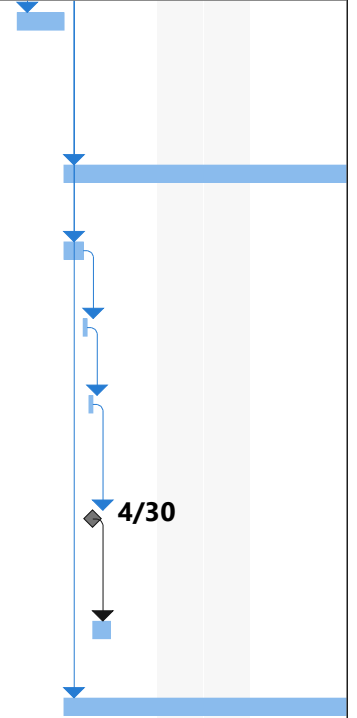
ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 26, '26							May 3, '26		
					S	M	T	W	T	F	S	S	M	T				
45			Apply the boom lift's first coat of paint.	2 days	Mon 4/27/26	Tue 4/28/26												
46			Allow the first coat to dry.	1 day	Wed 4/29/26	Wed 4/29/26	45											
47			Apply a second coat of paint.	1.5 days	Thu 4/30/26	Fri 5/1/26	46											
48			Touch up any missed areas.	0.5 days	Fri 5/1/26	Fri 5/1/26	47											
49			Quality Inspection (Gym Walls)	1 day	Thu 5/7/26	Thu 5/7/26	44											
50			Check coverage and complete it on the floor level.	0.5 days	Mon 4/27/26	Mon 4/27/26												
51			Check high places with a boom lift.	0.25 days	Mon 4/27/26	Mon 4/27/26	50											
52			Document completion	0.25 days	Mon 4/27/26	Mon 4/27/26	51											
53			Last Hallways Squares Painted.	8 days	Fri 5/8/26	Tue 5/19/26	49											
54			Still Hallway Surface Preparation	2 days	Mon 4/27/26	Tue 4/28/26												
55			Wipe, scrub, polish, and fix up the remaining wall of hallways.	1.5 days	Mon 4/27/26	Tue 4/28/26												



Project: Lyle Public Schools Inte Date: Mon 4/27/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 26, '26							May 3, '26		
					S	M	T	W	T	F	S	S	M	T				
56			Apply spot priming.	0.5 days	Tue 4/28/26	Tue 4/28/26	55											
57			Remaining Hallway Painting	4 days	Wed 4/29/26	Mon 5/4/26	54											
58			First coat of paint on the walls.	2 days	Mon 4/27/26	Tue 4/28/26												
59			Decorate the walls with a second coat of paint.	2 days	Wed 4/29/26	Thu 4/30/26	58											
60			Final Quality Inspection	1 day	Tue 5/5/26	Tue 5/5/26	57											
61			Carry out a comprehensive checkup on all the painted parts.	0.5 days	Mon 4/27/26	Mon 4/27/26												
62			Determine and meet touch-up requirements.	0.25 days	Mon 4/27/26	Mon 4/27/26	61											
63			Make sure that nothing is wrong.	0.25 days	Mon 4/27/26	Mon 4/27/26	62											
64			Project Management and	65 days	Mon 4/27/26	Fri 7/24/26												
65			Project Initiation	3 days	Mon 4/27/26	Wed 4/29/26												
66			Full project charter and project stakeholder communication	2 days	Mon 4/27/26	Tue 4/28/26												

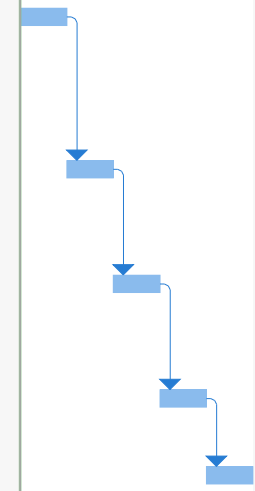
Project: Lyle Public Schools Inte Date: Mon 4/27/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			


ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 26, '26							May 3, '26		
					S	M	T	W	T	F	S	S	M	T				
67			Participate in the kickoff meeting with the painting contractor and	1 day	Wed 4/29/26	Wed 4/29/26	66											
68			Project Control and Monitoring.	55 days	Thu 4/30/26	Wed 7/15/26	65											
69			Weekly progress meetings	0.25 days	Thu 4/30/26	Thu 4/30/26	65											
70			Develop status reports weekly.	0.25 days	Thu 4/30/26	Thu 4/30/26	69											
71			Keep track of the budget vis-à-vis actual spending.	0.25 days	Thu 4/30/26	Thu 4/30/26	70											
72			Change requests to documents to be formally approved.	0 days	Thu 4/30/26	Thu 4/30/26	71											
73			Track schedule compliance.	0.25 days	Thu 4/30/26	Thu 4/30/26	72											
74			Quality Assurance	55 days	Thu 4/30/26	Wed 7/15/26	65											
75			Perform a quality check at each stage.	0.5 days	Thu 5/14/26	Thu 5/14/26	34,49,60											
76			Check adherence of contractor to commercial standards of	1 day	Thu 5/14/26	Fri 5/15/26	75											





Project: Lyle Public Schools Inte Date: Mon 4/27/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

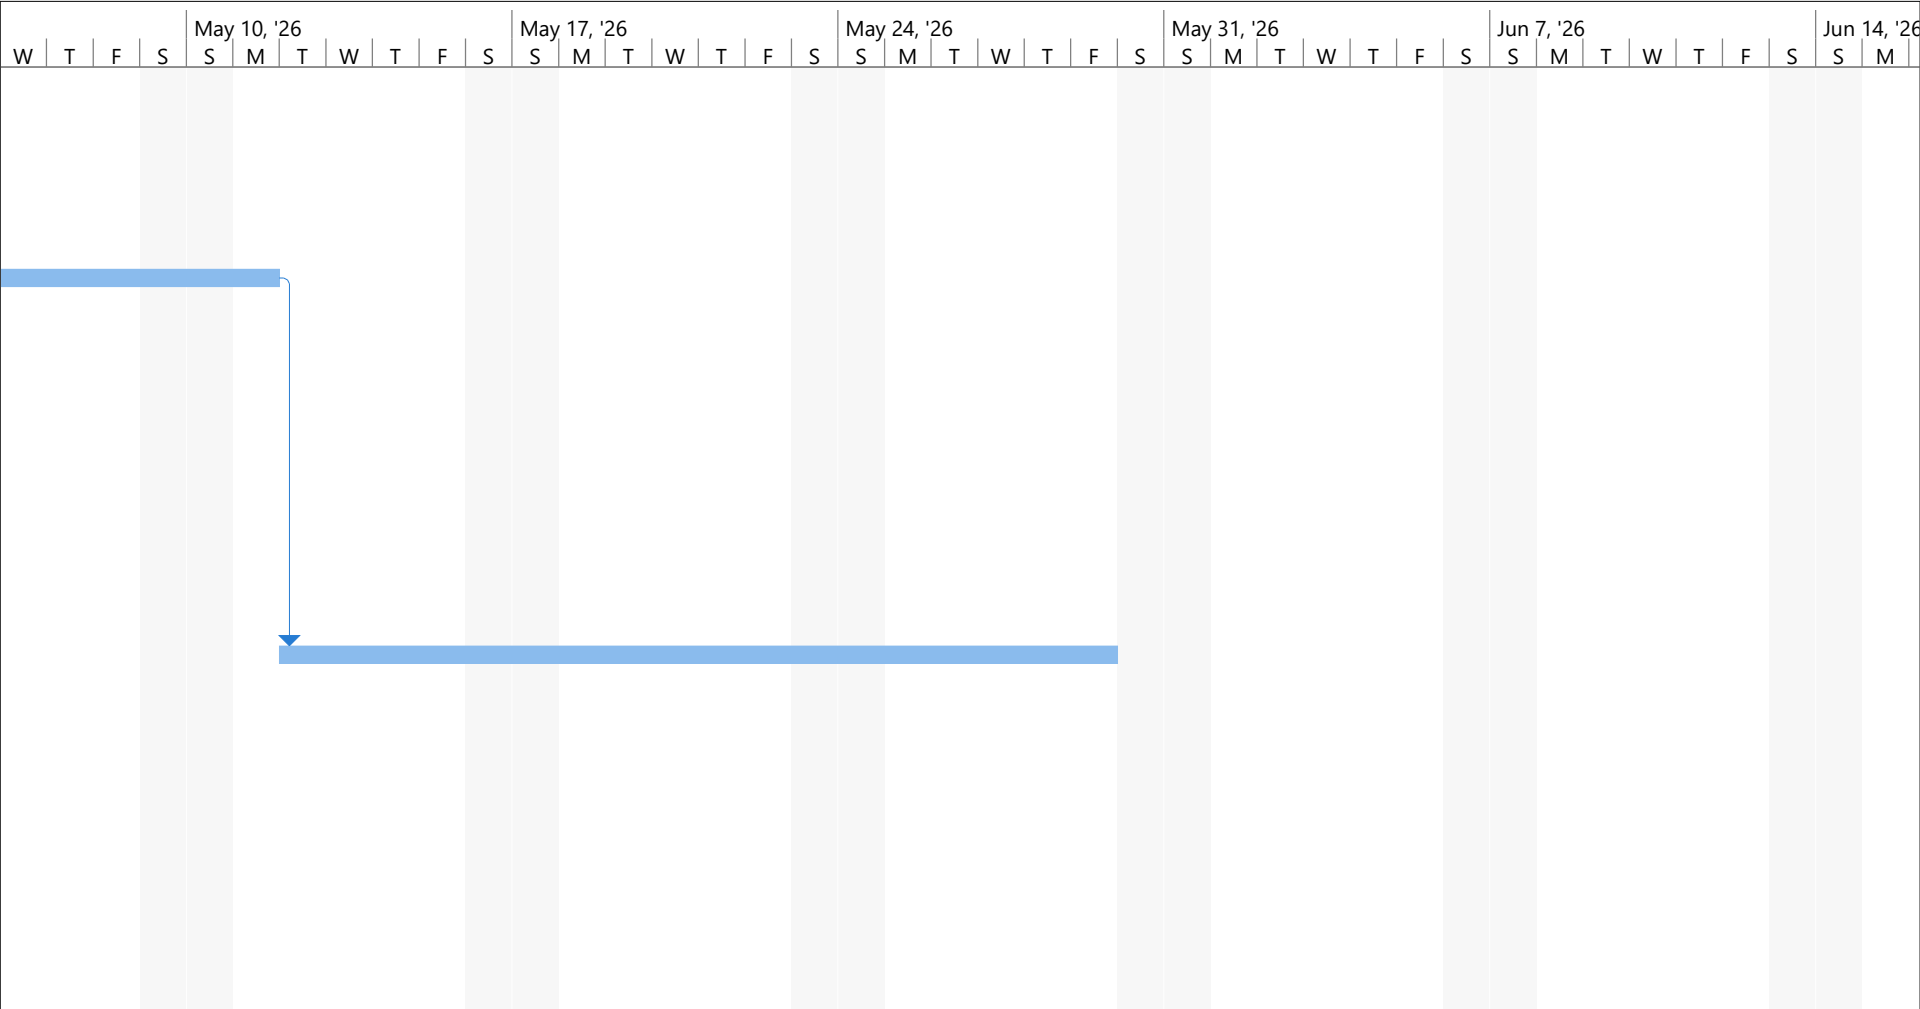
ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr 26, '26	S	M	T	W	T	F	S	May 3, '26	S	M	T
77			Inspecting the document results.	0.25 days	Fri 5/15/26	Fri 5/15/26	76													
78			Project Closeout	5 days	Thu 7/16/26	Wed 7/22/26	60,68,74													
79			Do a final walkthrough with school administration.	1 day?	Mon 4/27/26	Mon 4/27/26														
80			Get official project sign-off and acceptance.	1 day	Tue 4/28/26	Tue 4/28/26	79													
81			Prepare and store all the project documentation.	1 day	Wed 4/29/26	Wed 4/29/26	80													
82			Lessons learned from the meeting.	1 day	Thu 4/30/26	Thu 4/30/26	81													
83			Submit the final project report.	1 day	Fri 5/1/26	Fri 5/1/26	82													





Project: Lyle Public Schools Inte Date: Mon 4/27/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

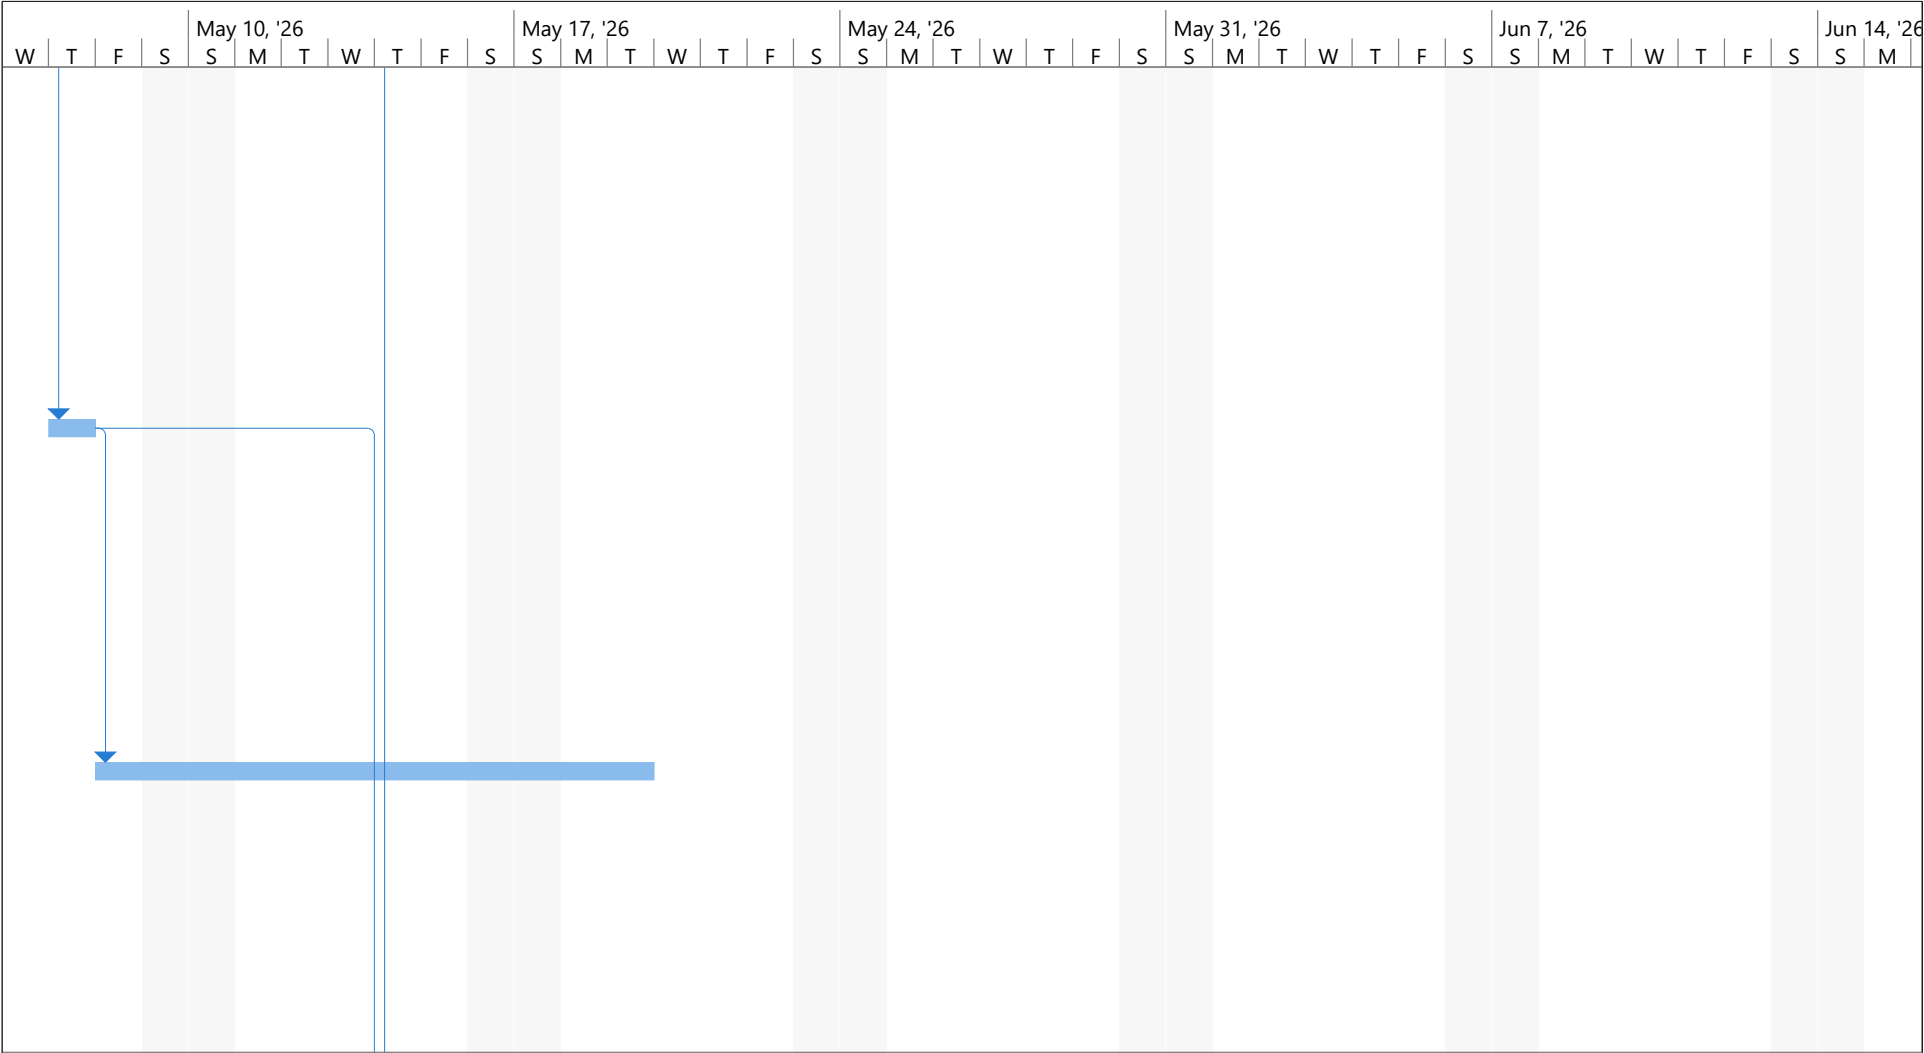


Project: Lyle Public Schools Inte Date: Mon 4/27/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

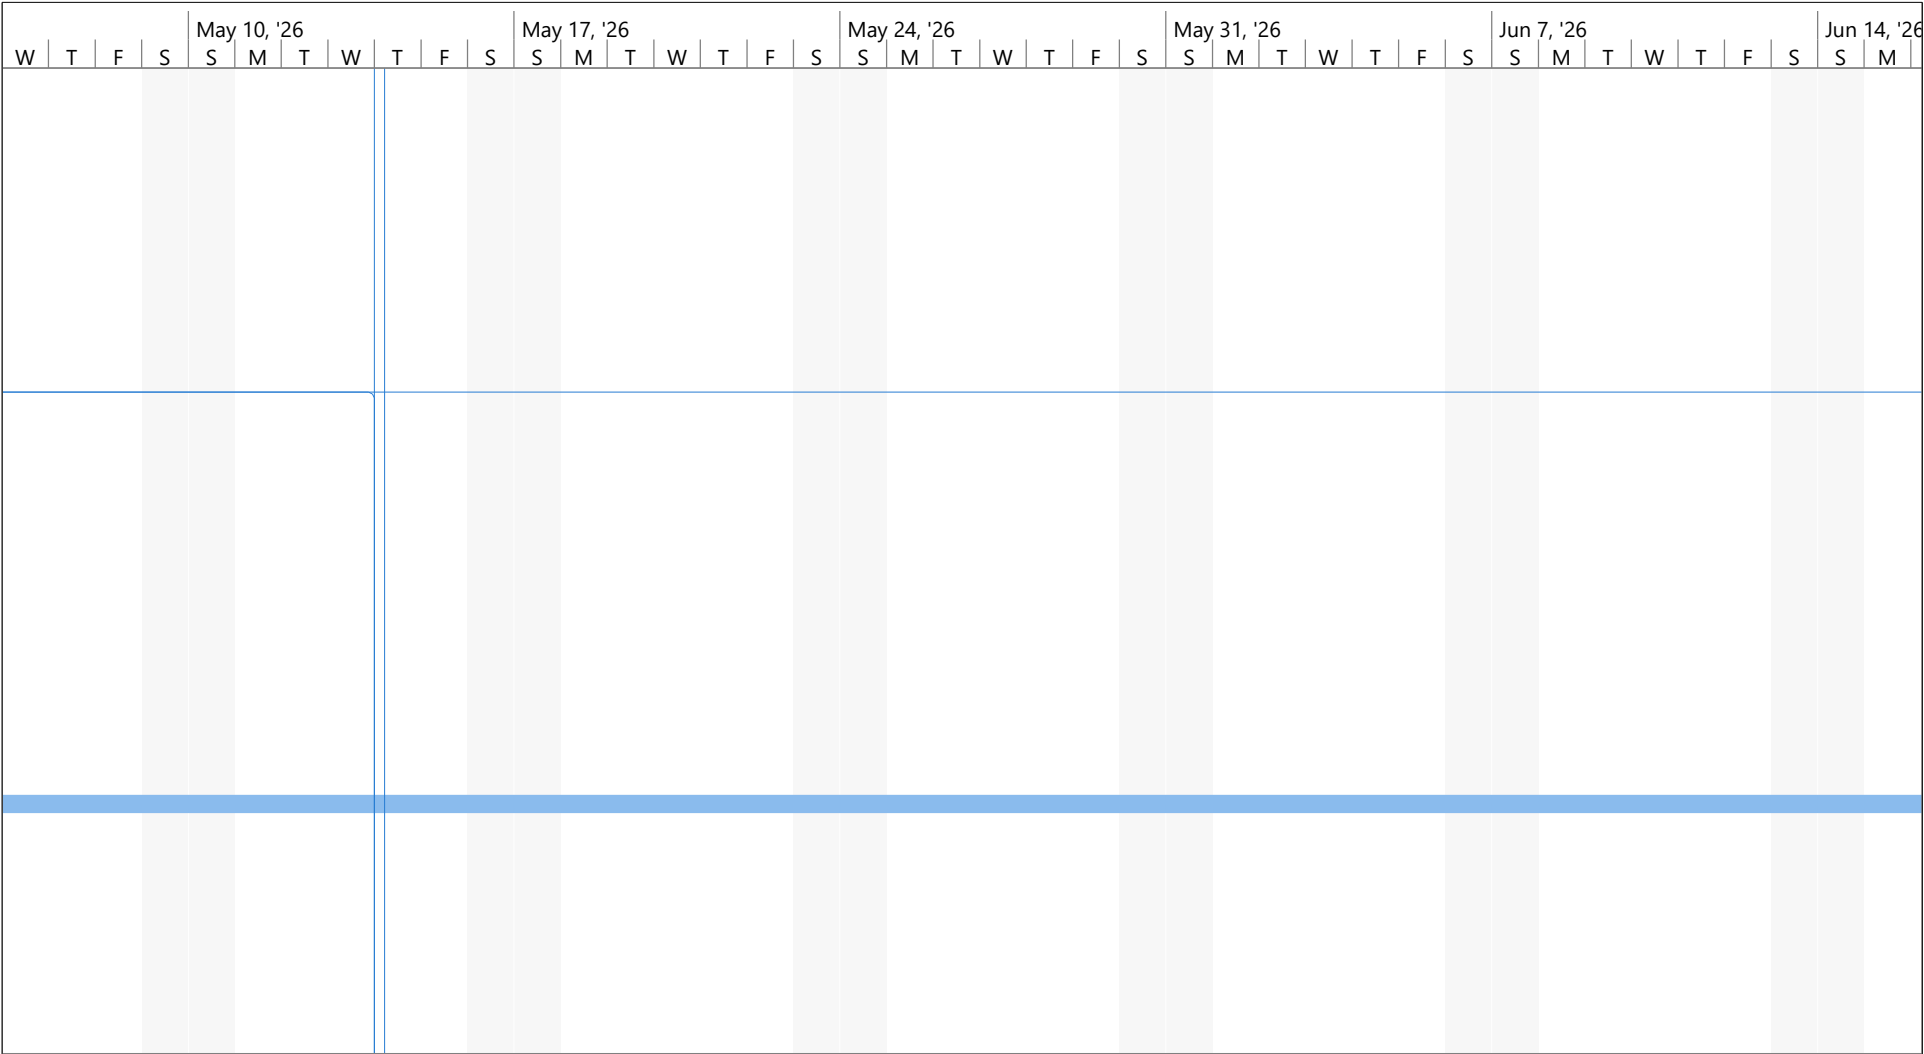


Project: Lyle Public Schools Inte Date: Mon 4/27/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

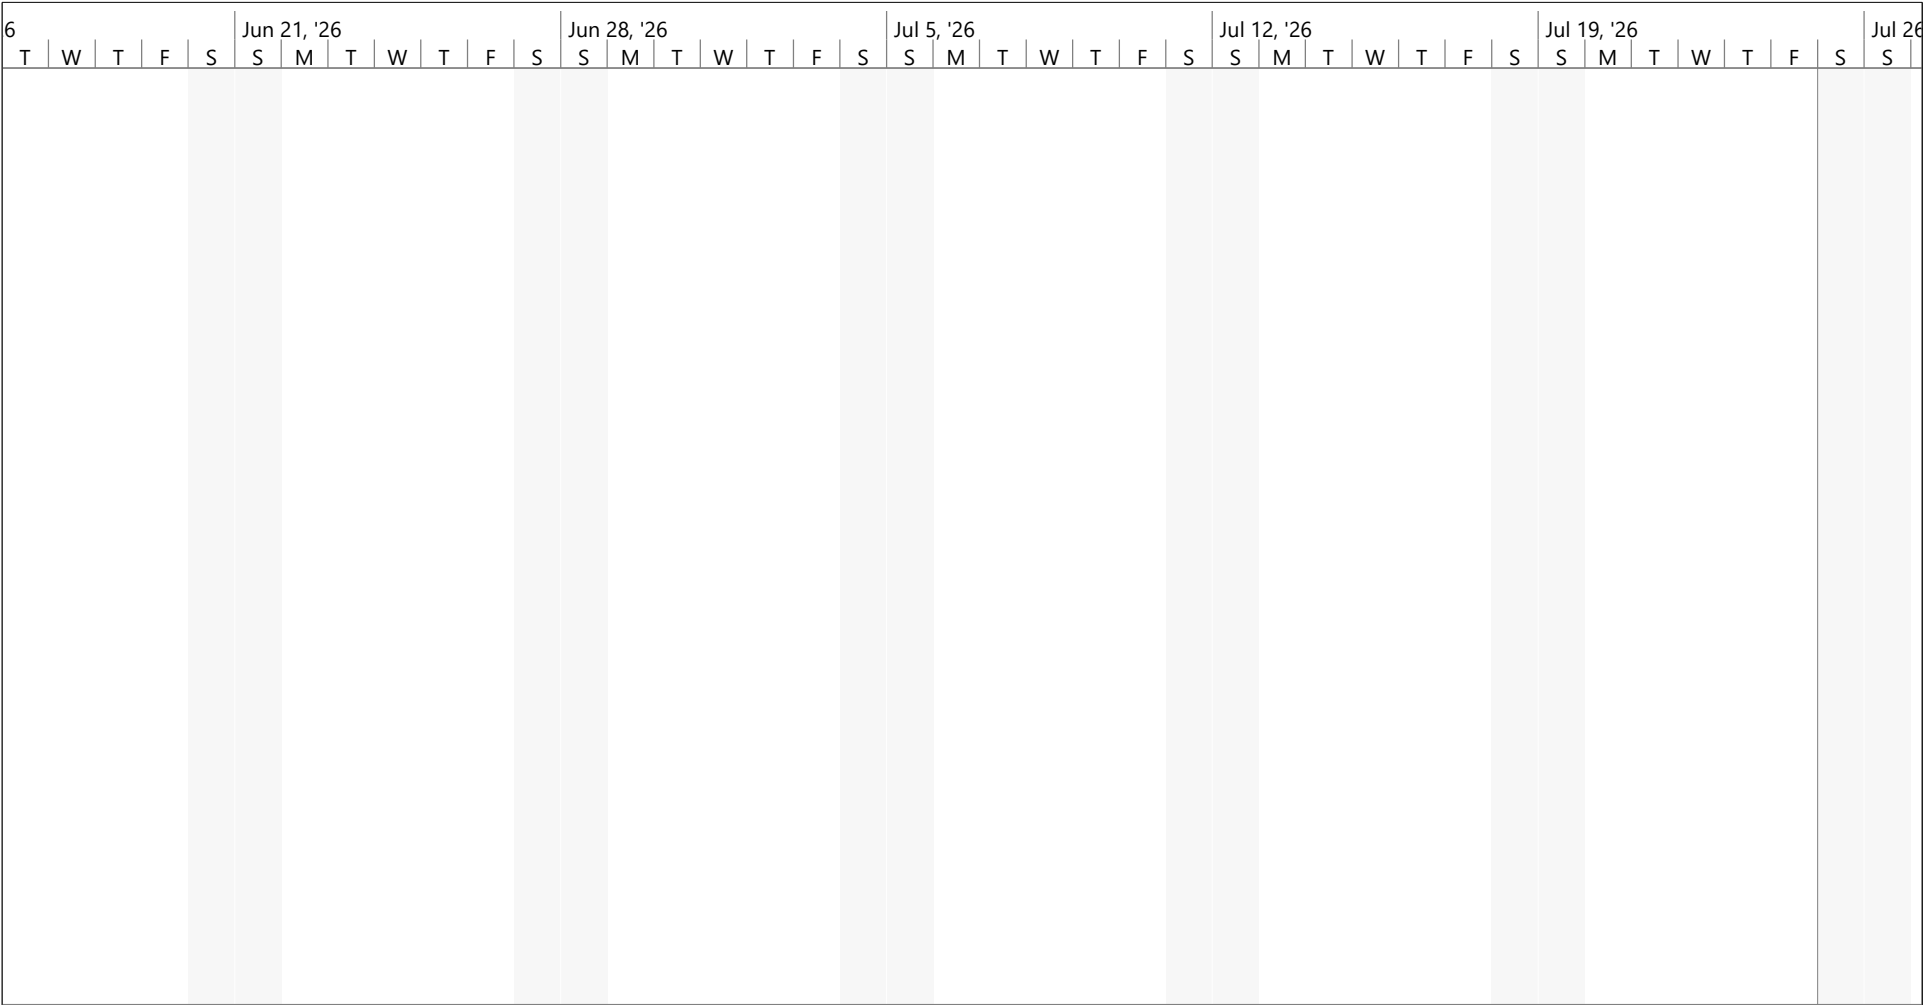






Project: Lyle Public Schools Inte Date: Mon 4/27/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



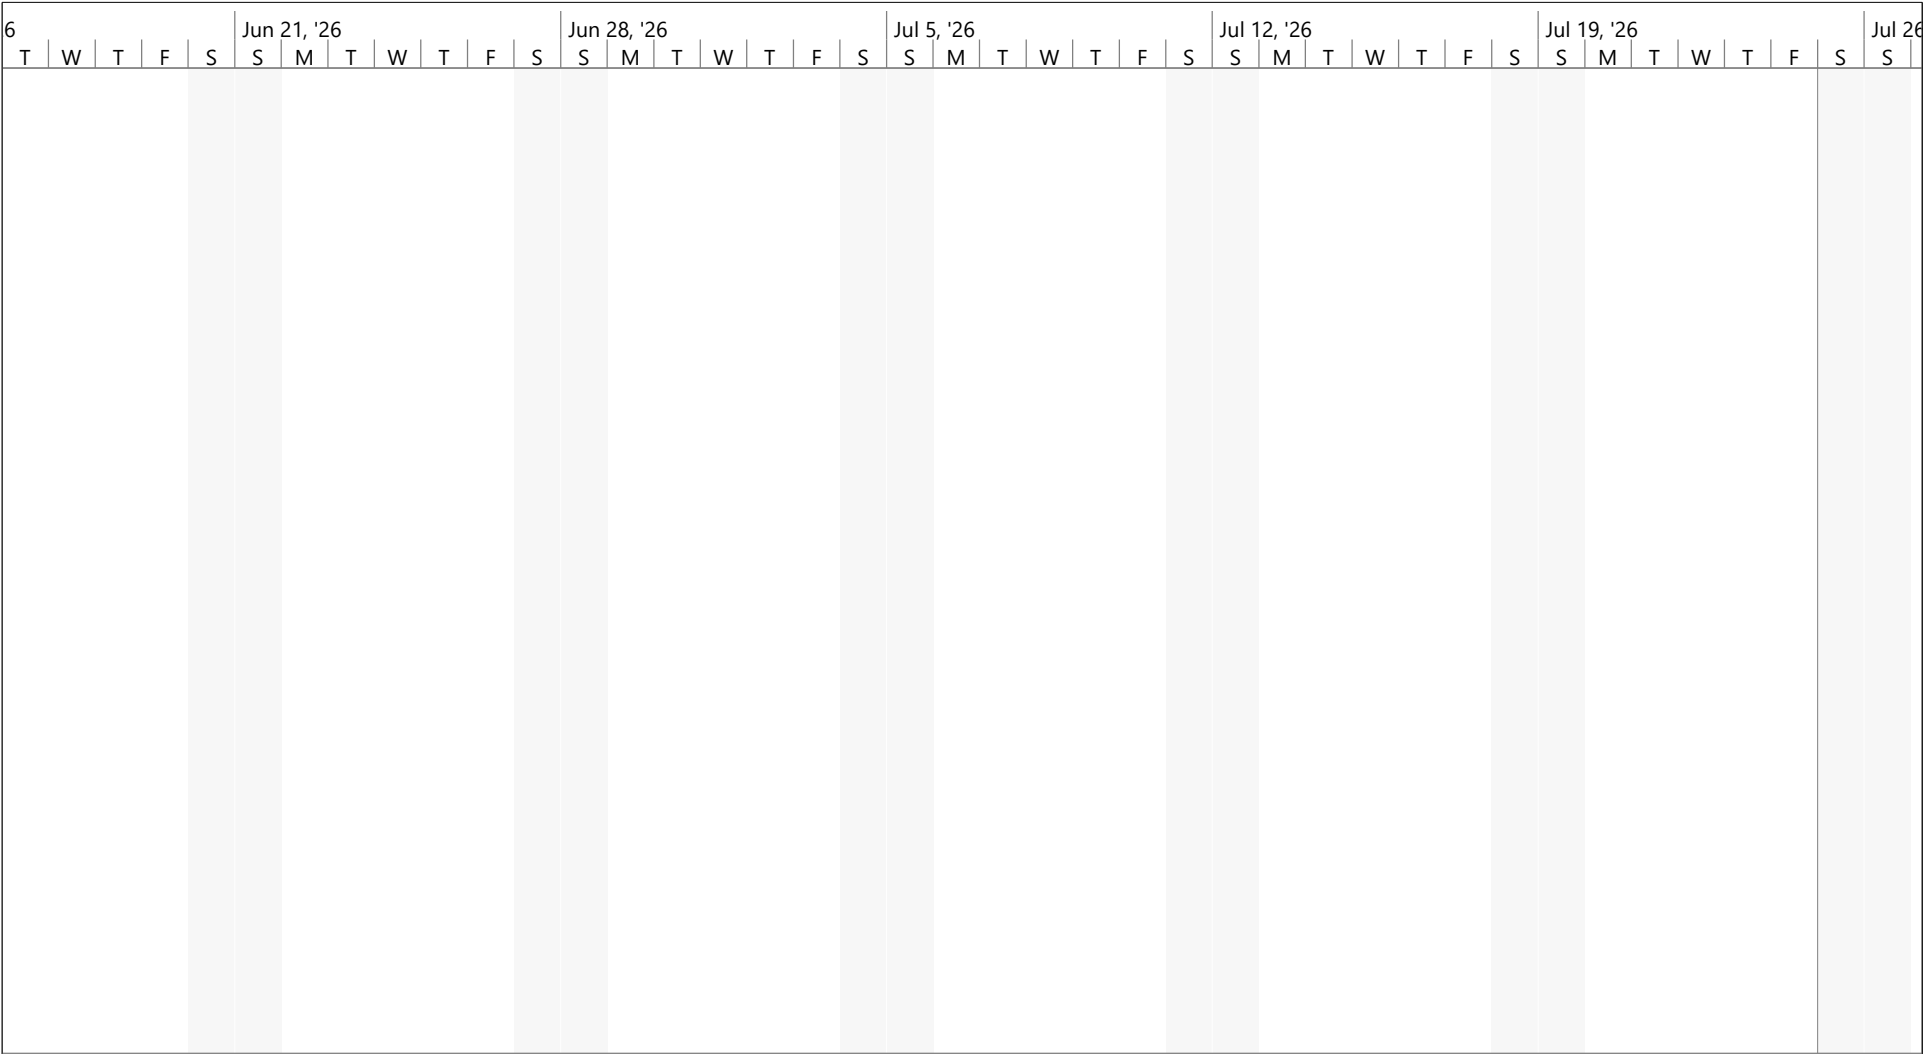
Project: Lyle Public Schools Inte Date: Mon 4/27/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			





Project: Lyle Public Schools Inte Date: Mon 4/27/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

6																																																																												
T	W	T	F	S	Jun 21, '26					S	M	T	W	T	F	S	Jun 28, '26					S	M	T	W	T	F	S	Jul 5, '26					S	M	T	W	T	F	S	Jul 12, '26					S	M	T	W	T	F	S	Jul 19, '26					S	M	T	W	T	F	S	Jul 26, '26					S	M	T	W	T	F	S

Project: Lyle Public Schools Inte Date: Mon 4/27/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: Lyle Public Schools Inte Date: Mon 4/27/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

